

SYSTEM UTILIZATION AND RELIABILITY MONTHLY REPORT

for the month ending
June 2014

<http://www.transcanada.com/customerexpress/2885.html>

Published date:
August 6th, 2014

Highlights This Month:

- No highlights for the month of June, 2014.

NOVA Gas Transmission Ltd.

TABLE OF CONTENTS

<u>MONTHLY FEATURES</u>	PAGE
Firm Transportation Service Contract Utilization	3
Design Capability Utilization	
Ft. McMurray Area – Flow Within	4
Kirby Area – Flow Within	5
North of Bens Lake – Flow Within	6
North & South of Bens Lake – Flow Within	7
Upper Peace River	8
Upper & Central Peace River	9
Peace River Design	10
Upstream James River	11
South & Alderson – Flow Within	12
Rimbey Nevis – Flow Within	13
Eastern Alberta Mainline (James River to Princess)	14
Medicine Hat - Flow Within	15
Eastern Alberta Mainline (Princess to Empress/McNeill)	16
Western Alberta Mainline (AB/BC & AB/Montana Borders)	17
Future Firm Transportation Service Availability	18
How to Use This Report	19

REFERENCES

NGTL Design Areas Map	20
NGTL Pipeline Segments Map	21
Definition of Terms	22

If you have any questions on the content of this report, contact Winston Cao at (403) 920-5315 or via fax at (403) 920-2357.

FIRM TRANSPORTATION SERVICE¹ CONTRACT UTILIZATION³
By NGTL Pipeline Segments
June 2014

Segment	Contract	Delivery		Receipt	
		Utilization	Jun CD (TJ/d)	Utilization	Jun CD (MMcf/d)
UPRM	FT	5%	22.8	86%	57
	FT + IT ²	12%		103%	
PRLL	FT	27%	47.2	95%	90
	FT + IT	28%		125%	
NWML	FT	11%	8.1	60%	561
	FT + IT	11%		64%	
GRDL	FT	8%	9.0	76%	1,852
	FT + IT	8%		78%	
WRSY	FT	0%	0.0	90%	16
	FT + IT	0%		137%	
WAEX	FT	7%	13.7	65%	365
	FT + IT	58%		81%	
JUDY	FT	25%	33.8	88%	63
	FT + IT	29%		133%	
GPML	FT	21%	168.1	82%	2,944
	FT + IT	25%		90%	
CENT	FT	57%	1.3	85%	1,001
	FT + IT	57%		107%	
LPOL	FT	21%	76.9	89%	705
	FT + IT	32%		110%	
WGAT	FT	49%	3,425.2	81%	318
	FT + IT	49%		96%	
ALEG	FT	33%	345.7	96%	811
	FT + IT	42%		125%	
SLAT	FT	15%	179.0	92%	222
	FT + IT	16%		112%	
MLAT	FT	65%	262.8	80%	195
	FT + IT	78%		95%	
BLEG	FT	40%	138.5	91%	593
	FT + IT	41%		101%	
EGAT	FT	97%	4,322.6	77%	33
	FT + IT	106%		100%	
MRTN	FT	17%	36.4	77%	61
	FT + IT	20%		138%	
LIEG	FT	74%	1,254.7	46%	29
	FT + IT	81%		160%	
KIRB	FT	63%	1,149.0	72%	37
	FT + IT	63%		139%	
SMHI	FT	39%	12.0	89%	32
	FT + IT	39%		137%	
REDL	FT	0%	10.0	82%	40
	FT + IT	4%		115%	
COLD	FT	48%	88.6	95%	18
	FT + IT	87%		141%	
EDM	FT	31%	1,746.7	90%	54
	FT + IT	32%		122%	
NLAT	FT	13%	15.9	97%	122
	FT + IT	13%		143%	
WAIN	FT	5%	0.4	74%	6
	FT + IT	5%		186%	
ELAT	FT	75%	268.9	93%	116
	FT + IT	79%		146%	
TOTAL SYSTEM	FT	64%	13,637.3	82%	10,342
	FT + IT	69%		96%	

*NOTE:



1. FT includes all receipt and delivery Firm Transportation Services: FTR, FTRN, LRS, FTD1, FTD2, FTD3 and FTP.

2. IT includes receipt and delivery Interruptible Services: IT-R and IT-D respectively.

3. Utilization data is based on billed monthly volumes. Percent utilization calculated as FT and FT + IT billed volumes divided by applicable receipt or delivery Contract level.

DESIGN CAPABILITY UTILIZATION



FT. McMURRAY AREA – FLOW WITHIN

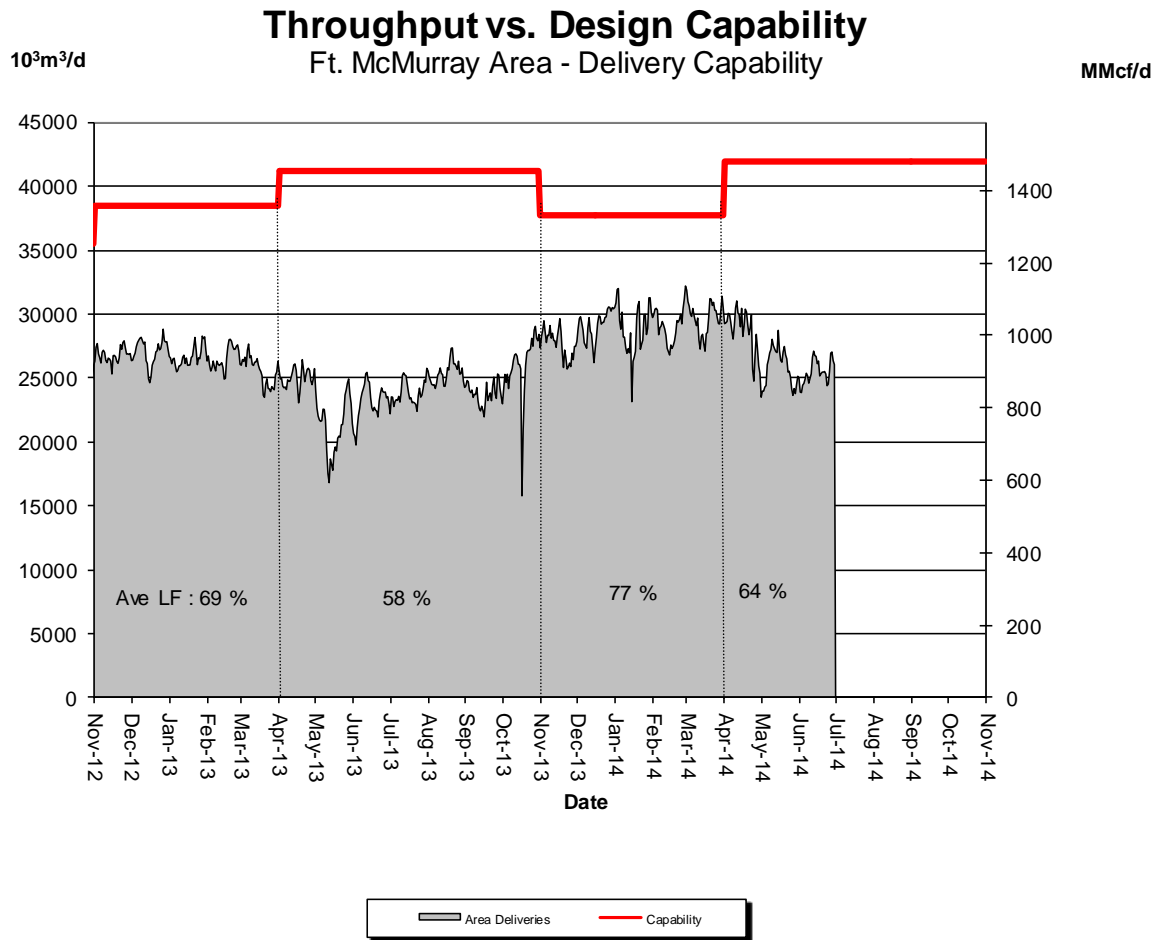

% Design Capability Utilization						
Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Jan	Feb	Mar	Apr	May	Jun
	77	77	79	69	62	61



DESIGN CAPABILITY UTILIZATION

KIRBY AREA – FLOW WITHIN

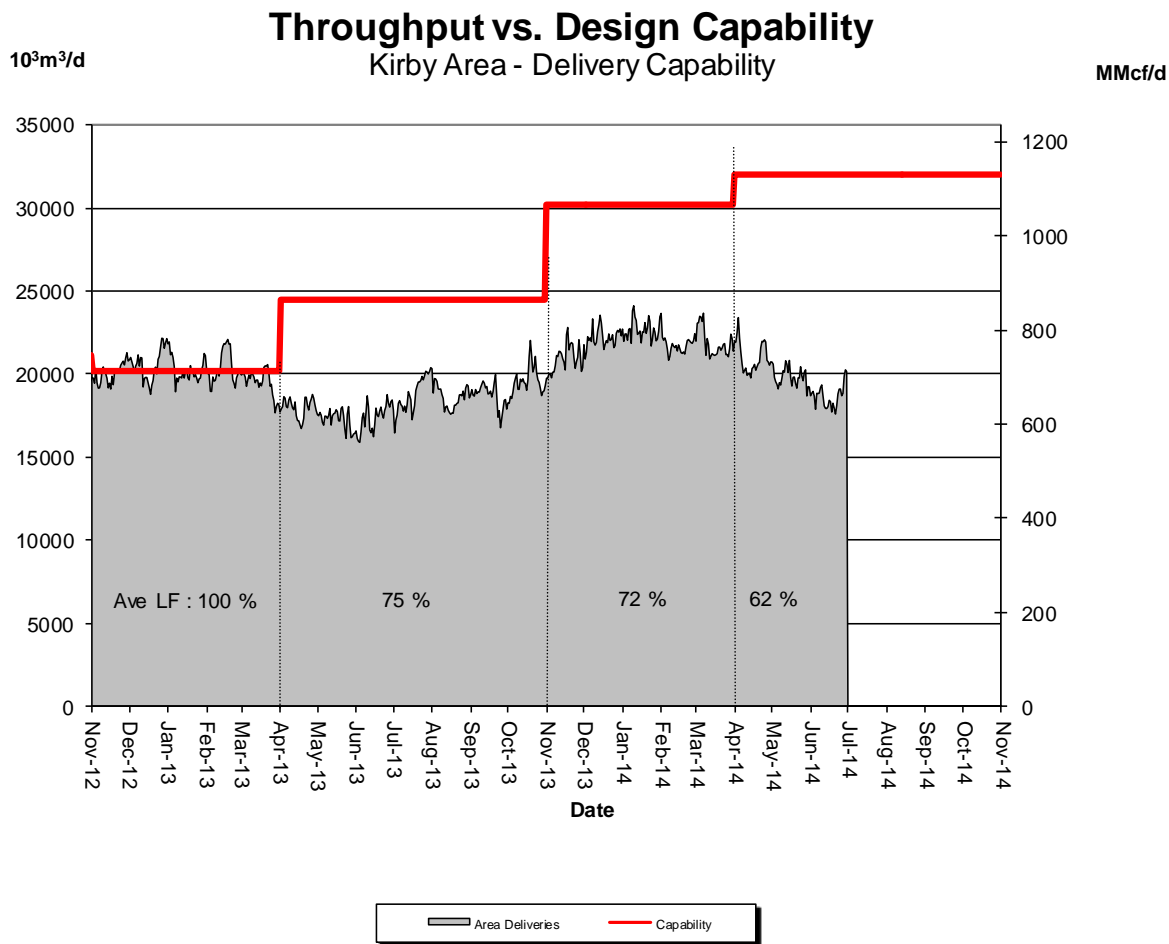

% Design Capability Utilization Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Jan	Feb	Mar	Apr	May	Jun
	75	72	72	66	62	58



DESIGN CAPABILITY UTILIZATION NORTH OF BENS LAKE – FLOW WITHIN

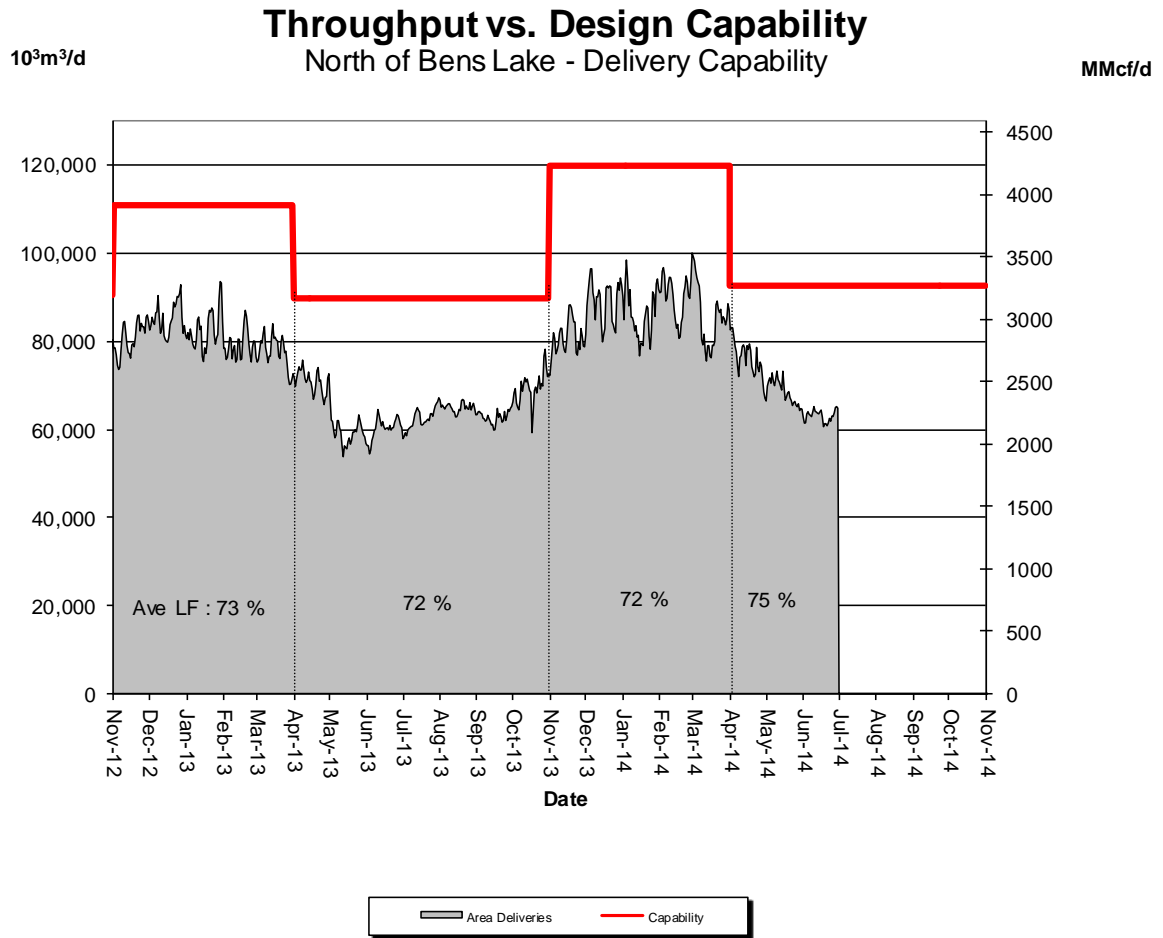

% Design Capability Utilization Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Jan	Feb	Mar	Apr	May	Jun
	72	75	71	82	74	68


DESIGN CAPABILITY UTILIZATION

NORTH & SOUTH OF BENS LAKE – FLOW WITHIN

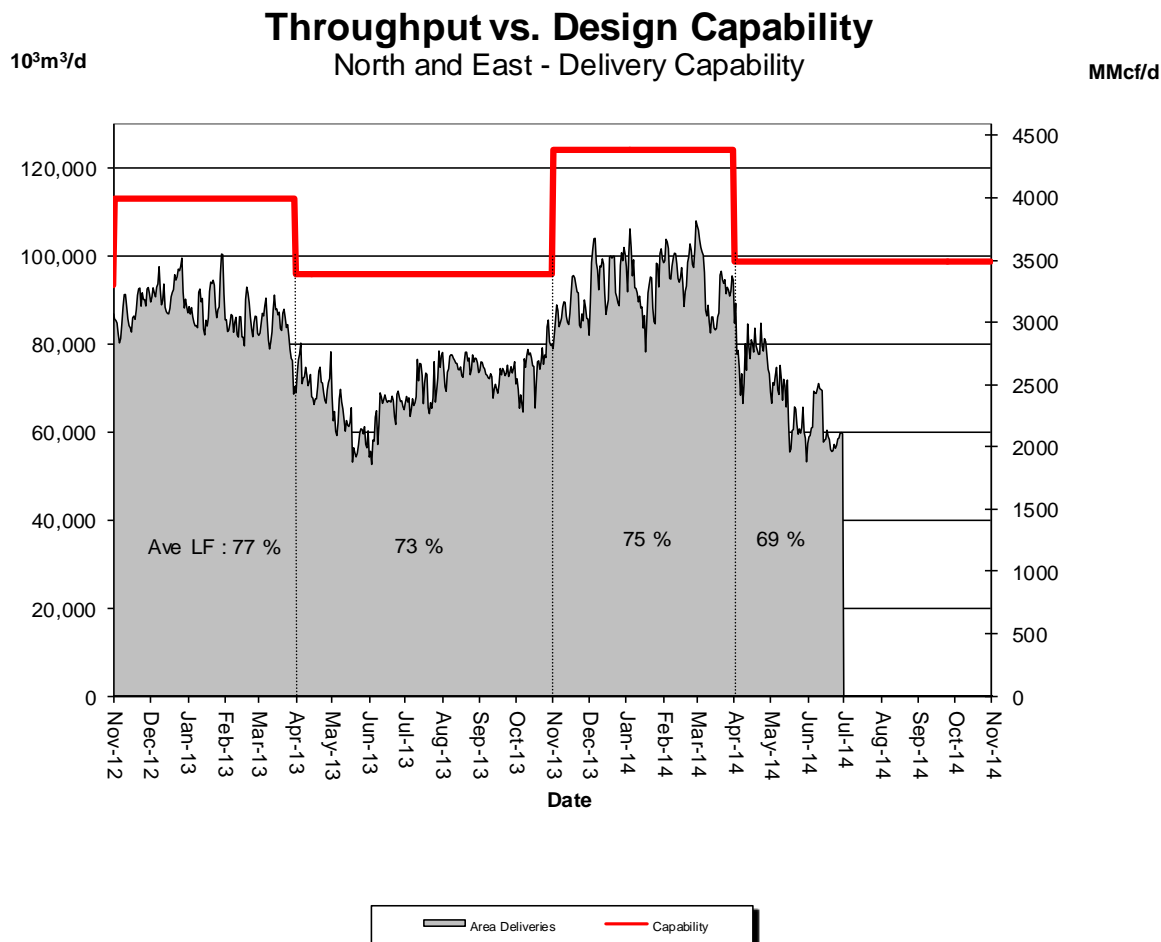



% Design Capability Utilization Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Jan	Feb	Mar	Apr	May	Jun
	75	79	74	79	66	62

DESIGN CAPABILITY UTILIZATION UPPER PEACE RIVER

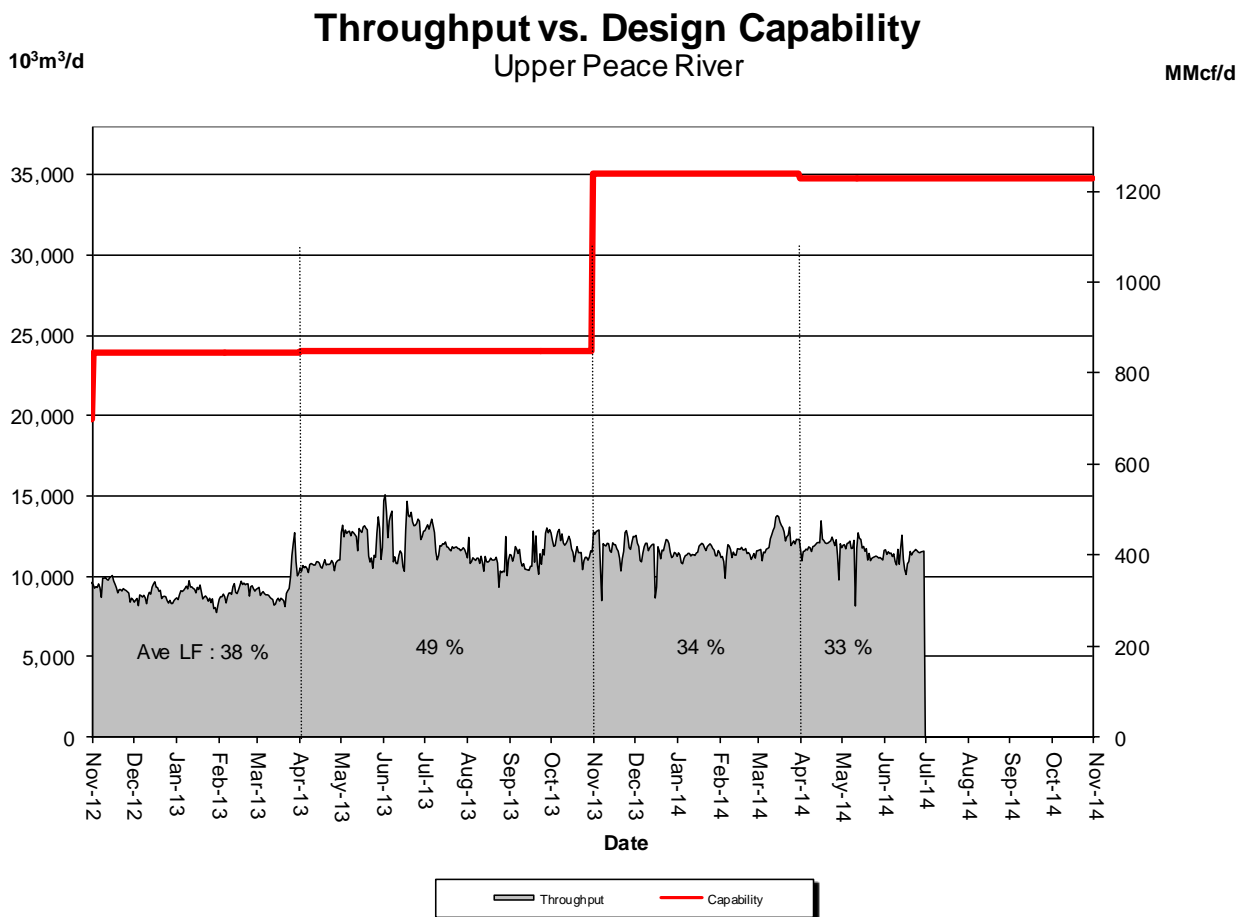

% Design Capability Utilization Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Jan	Feb	Mar	Apr	May	Jun
	33	33	35	34	33	33

DESIGN CAPABILITY UTILIZATION UPPER and CENTRAL PEACE RIVER

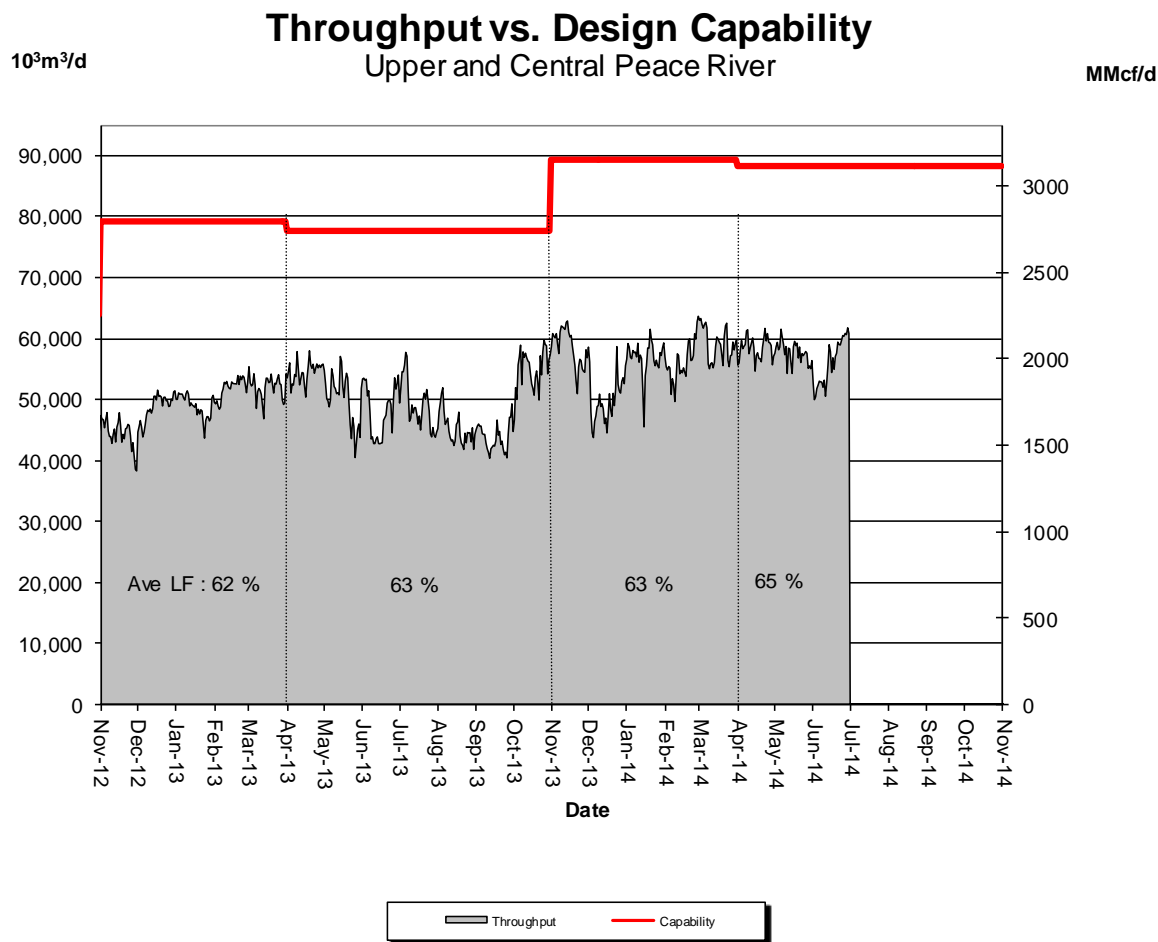



% Design Capability Utilization Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Jan	Feb	Mar	Apr	May	Jun
	64	63	66	66	65	63

DESIGN CAPABILITY UTILIZATION

PEACE RIVER DESIGN



(Upper, Central and Lower Peace River)

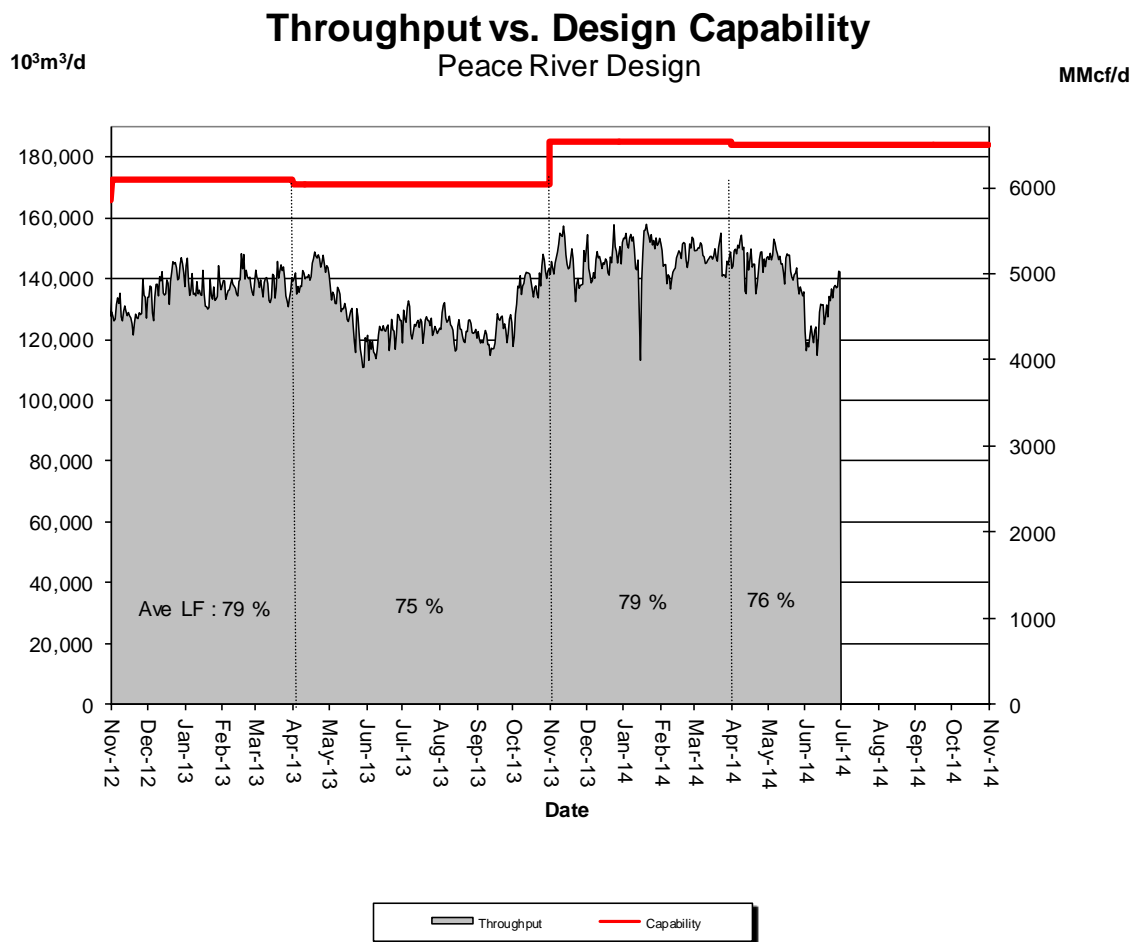

% Design Capability Utilization Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Jan	Feb	Mar	Apr	May	Jun
	81	79	80	79	78	70



DESIGN CAPABILITY UTILIZATION UPSTREAM JAMES RIVER

(Edson Mainline, Peace River Design and Marten Hills)

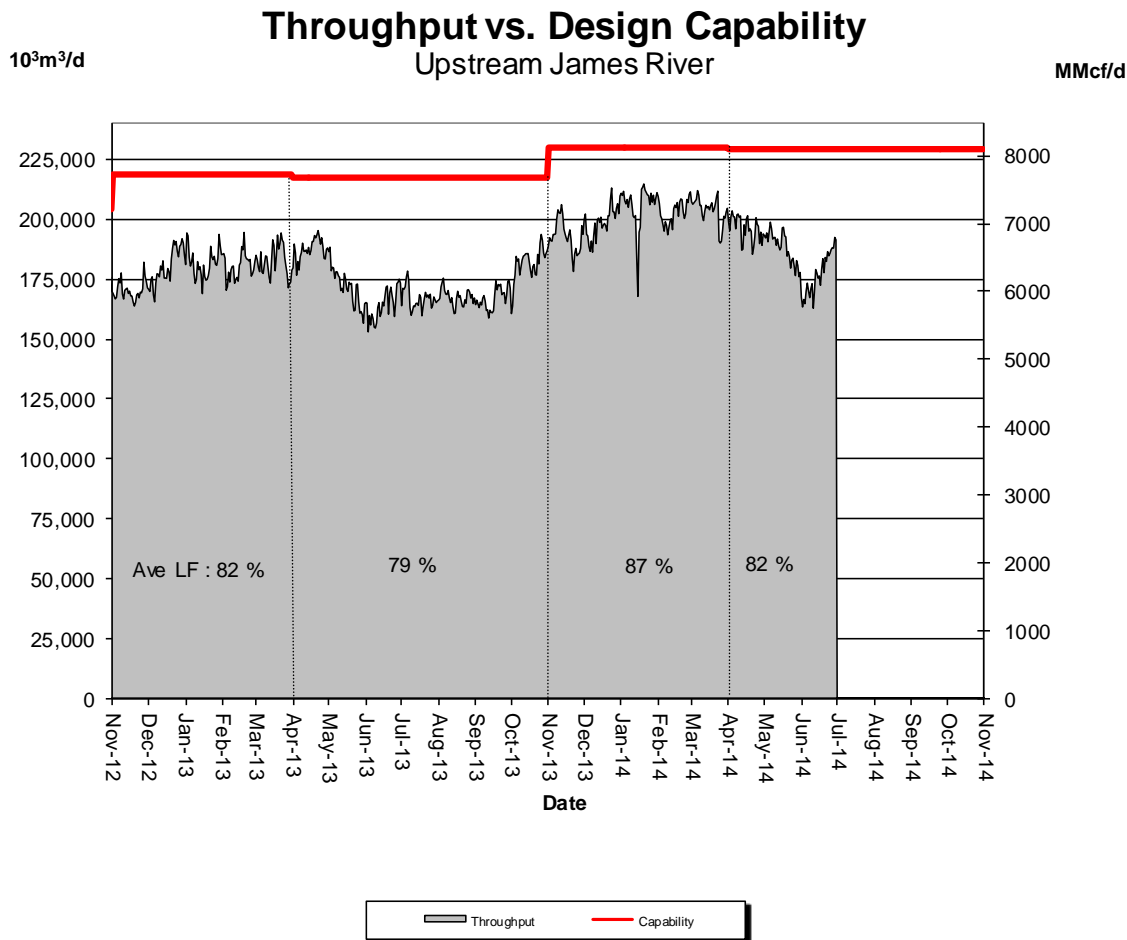

% Design Capability Utilization Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Jan	Feb	Mar	Apr	May	Jun
	90	88	89	86	82	77



DESIGN CAPABILITY UTILIZATION SOUTH and ALDERSON – FLOW WITHIN

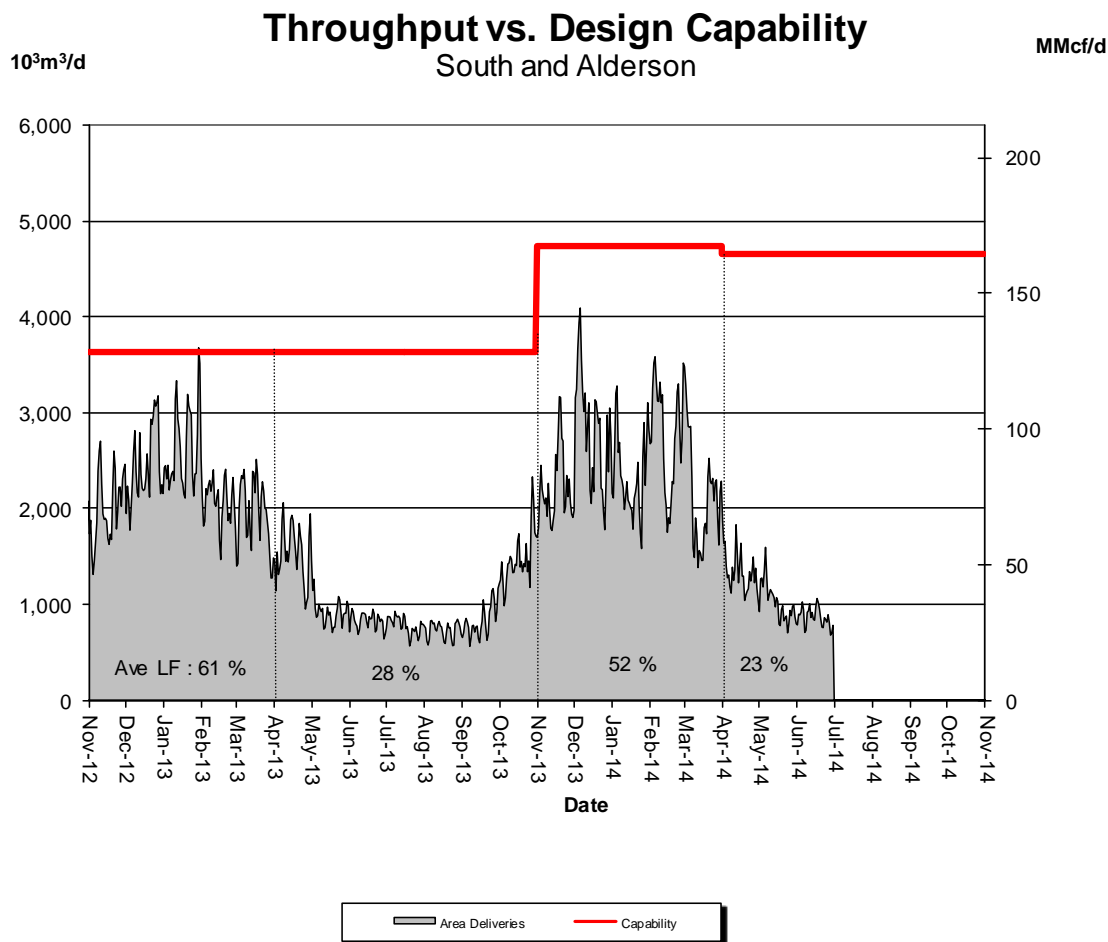

% Design Capability Utilization Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Jan	Feb	Mar	Apr	May	Jun
	49	58	45	29	22	19



DESIGN CAPABILITY UTILIZATION

RIMBEY-NEVIS – FLOW WITHIN

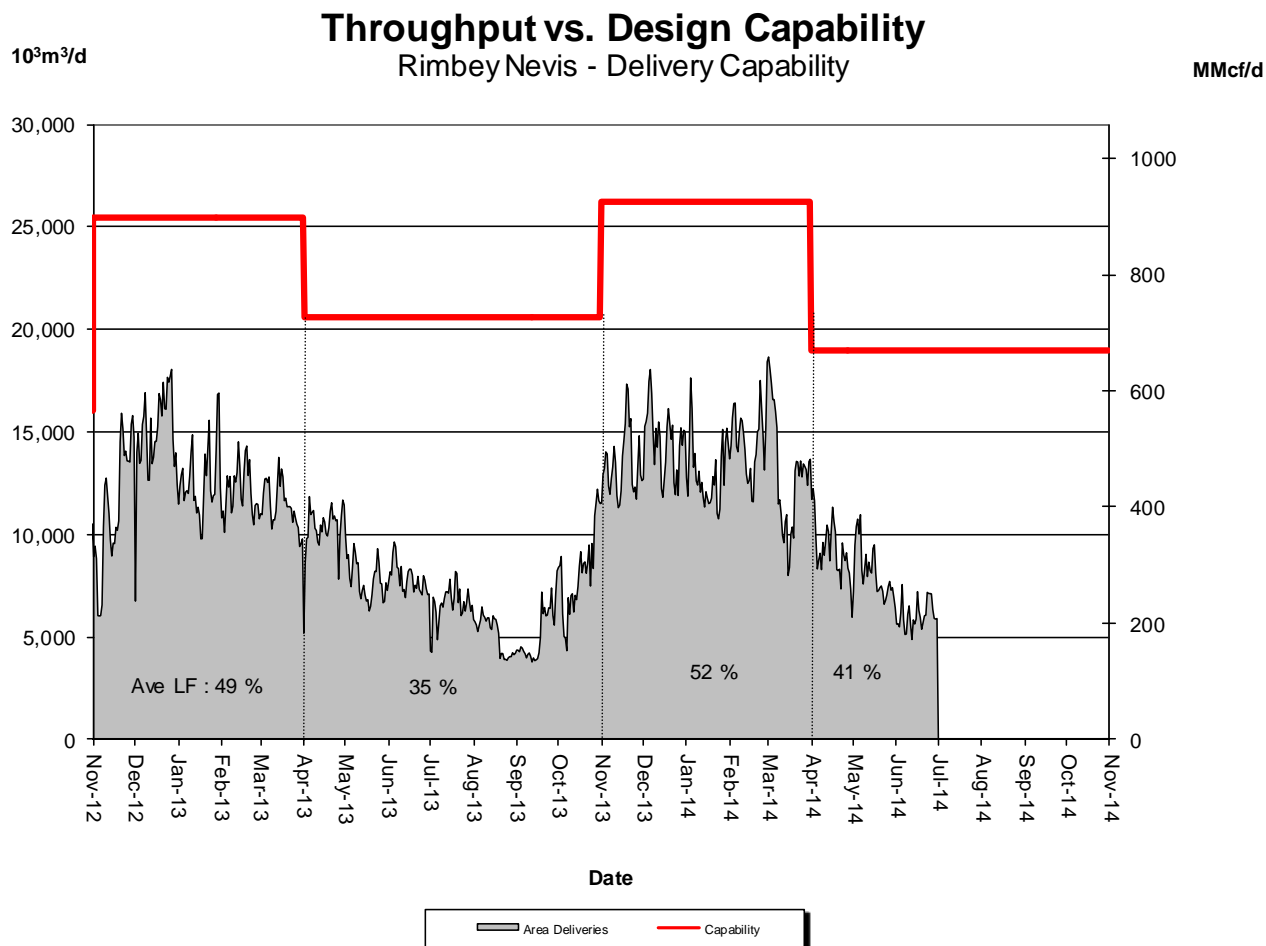

% Design Capability Utilization Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Jan	Feb	Mar	Apr	May	Jun
	49	56	49	49	43	32



DESIGN CAPABILITY UTILIZATION EASTERN ALBERTA MAINLINE (James River to Princess)

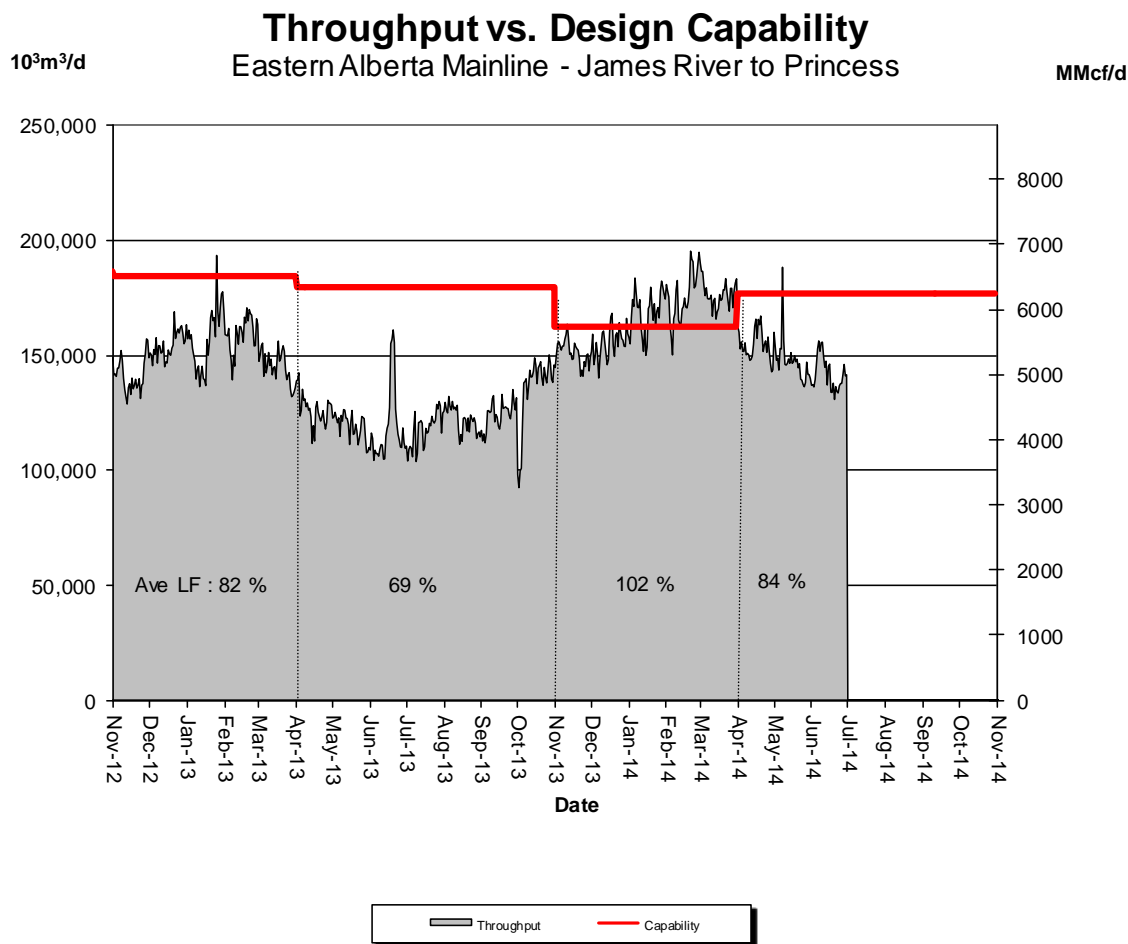

% Design Capability Utilization Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Jan	Feb	Mar	Apr	May	Jun
	104	108	109	87	83	80



DESIGN CAPABILITY UTILIZATION

MEDICINE HAT – FLOW WITHIN

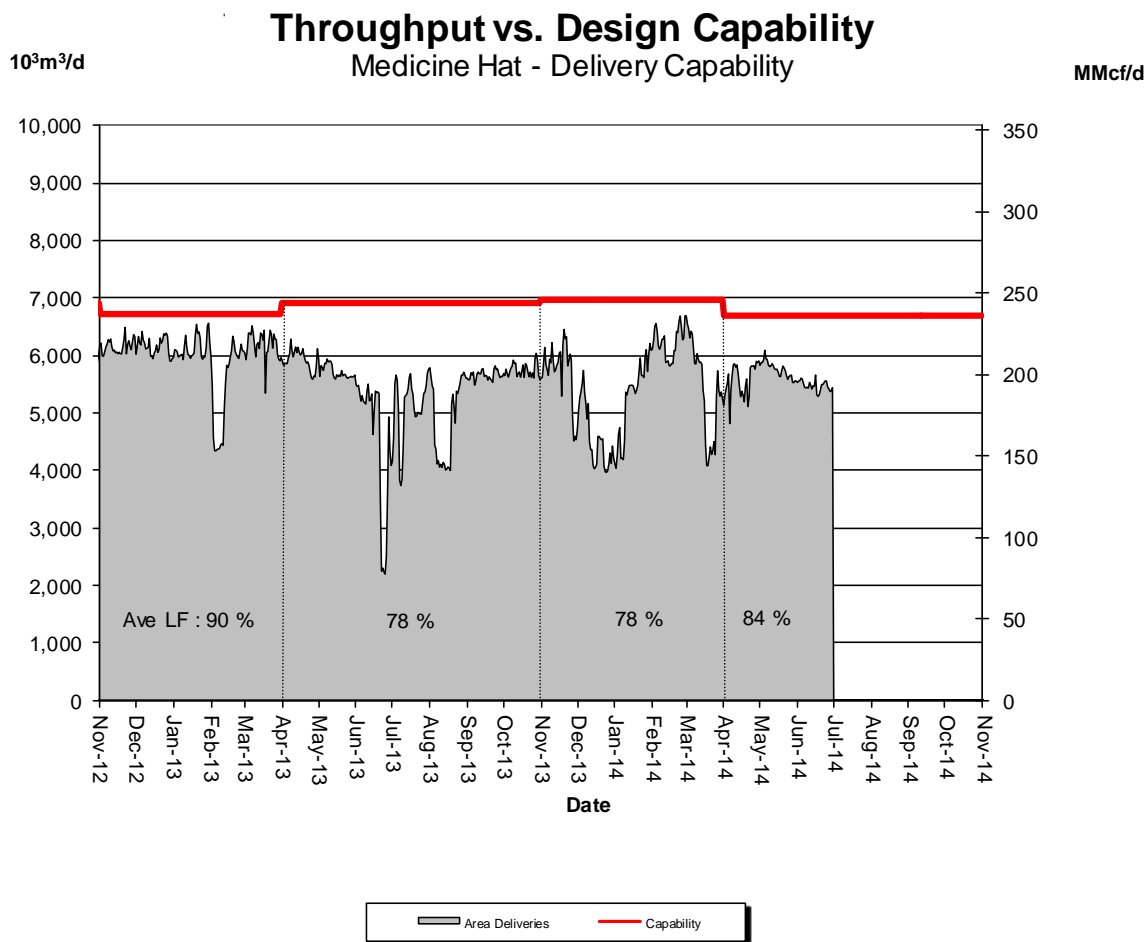



% Design Capability Utilization Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Jan	Feb	Mar	Apr	May	Jun
	76	89	78	83	86	82

DESIGN CAPABILITY UTILIZATION EASTERN ALBERTA MAINLINE (Princess to Empress / McNeill)

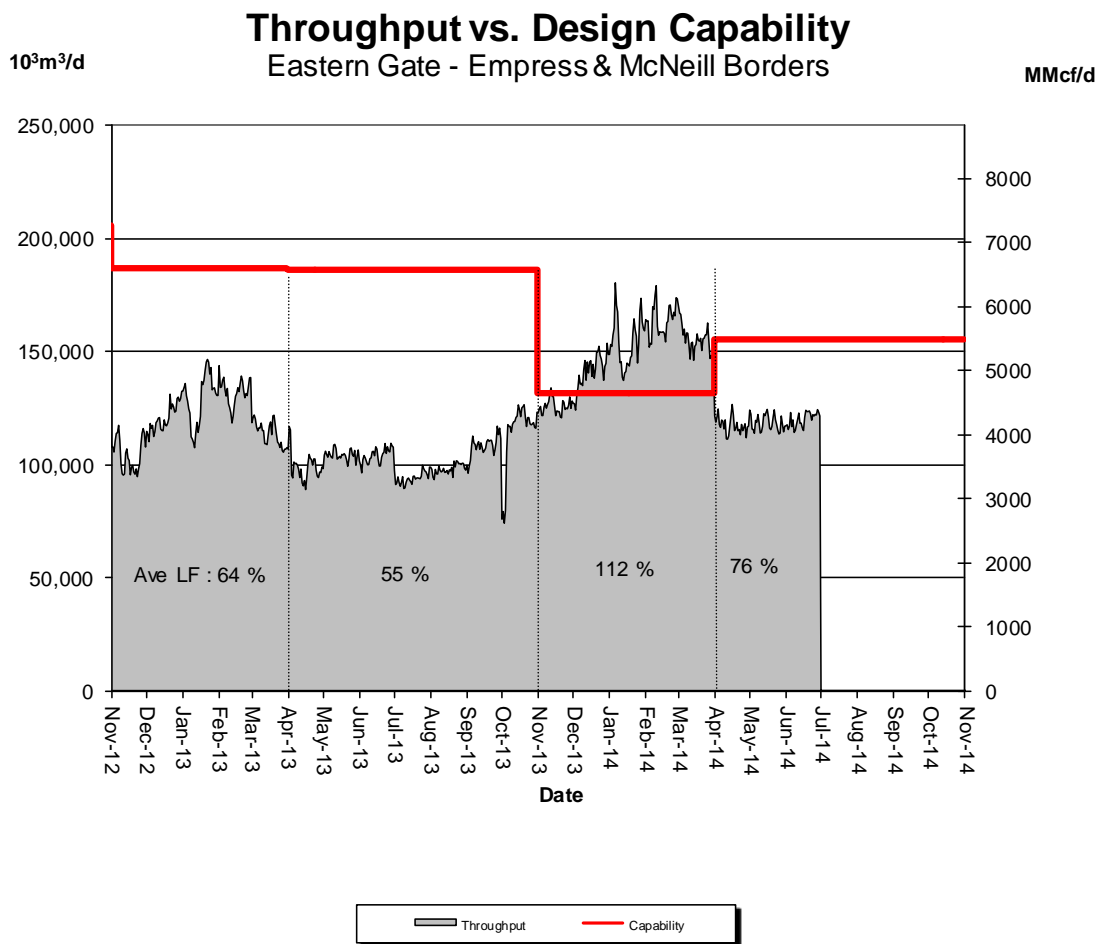

% Design Capability Utilization Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Jan	Feb	Mar	Apr	May	Jun
	117	124	118	75	76	77

DESIGN CAPABILITY UTILIZATION WESTERN ALBERTA MAINLINE (Alberta/B.C. and Alberta/Montana Borders)

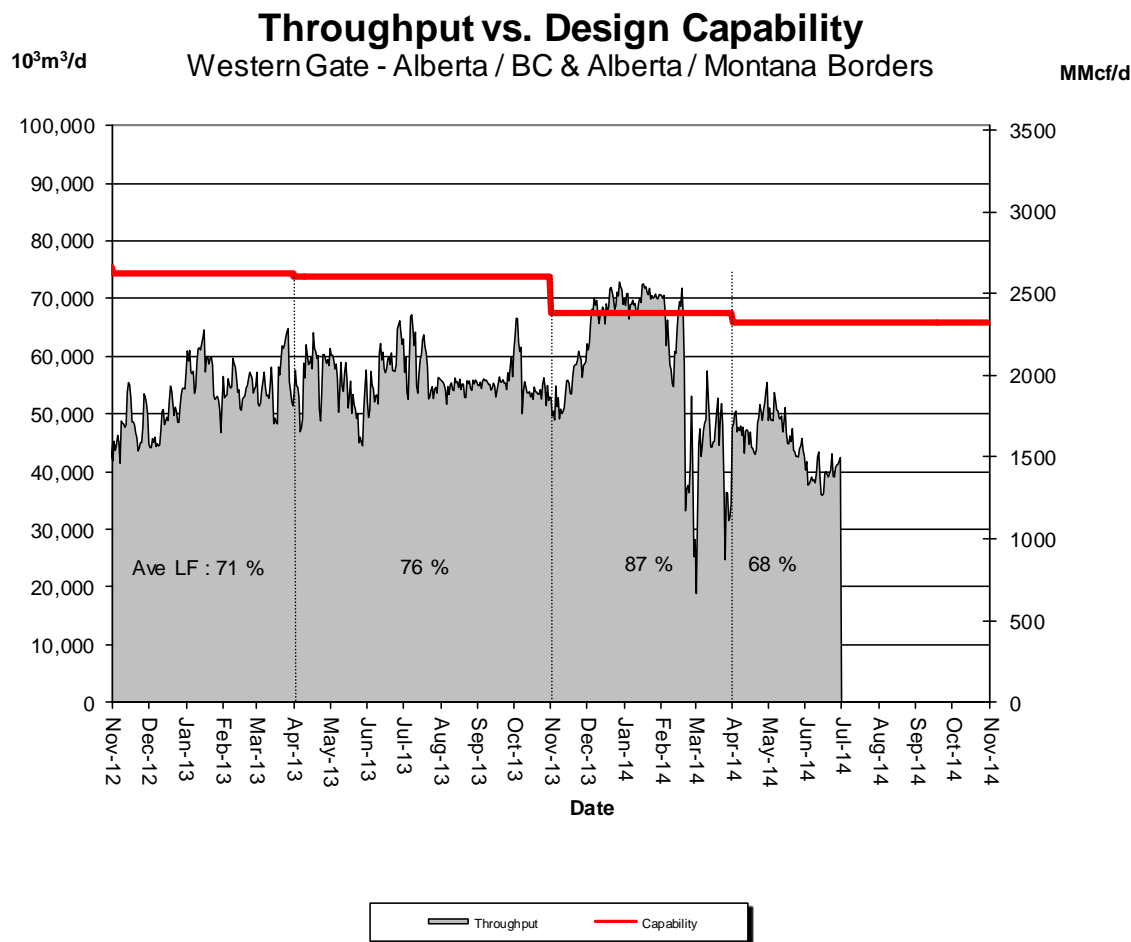

% Design Capability Utilization						
Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Jan	Feb	Mar	Apr	May	Jun
	104	84	63	73	71	60

FUTURE FIRM TRANSPORTATION SERVICE AVAILABILITY (MAINLINE RESTRICTIONS)

Receipt and Delivery Firm Transportation Guidelines

Firm Transportation Location	Authorize Firm Transportation Service By	To Ensure Firm Transportation Service By
Summer construction (generally south of Edmonton)	November 2014	November 2016
Winter construction (generally north of Edmonton)	November 2014	April 2017

Estimated Firm Transportation Service Availability

Please refer to the following web site for
current FT-R / FT-D Availability Maps:

<http://www.transcanada.com/customerexpress/2801.html>

➤ If your needs for firm transportation service arise after the above dates to “Authorize Firm Transportation Service By”, NGTL will evaluate your new receipt firm transportation service or firm service transfer requests on a date-stamped basis.

Please consult with your Customer Sales Representative to discuss your Firm Transportation Service needs.

HOW TO USE THIS REPORT

Overview

This report contains recent historical information on the level of utilization of firm transportation Service Agreements on the NGTL system, relative usage of interruptible service, level of utilization of design pipeline capacity, and the availability of transportation services as an indication of system reliability.

Data is reported either by *Pipeline Segment* (26 on the system) or *Design Area* (13 on the system). Maps of both are included in the reference section.

Firm Transportation Service Contract Utilization

The Firm Transportation Service Contract Utilization report shows the percent utilization for each of the 26 NGTL pipeline segments and 3 major export delivery points comprising the total system. The utilization data is based on billed monthly volumes. Percent utilization is calculated as firm transportation service and firm transportation service + interruptible service divided by applicable receipt or delivery contract level. Historical Data involving billed volumes lags the current date by approximately two months.

Design Capability Utilization

The load factor/segment flow graphs show actual flow versus design capability values for various NGTL system areas. The graphs also show seasonal (winter/summer) design capability and average load factors (LF) for each season. Load factors are obtained by comparing the dominant flow condition in each of the Alberta design areas against the corresponding design capability. Consequently, design capability utilization is measured as Average Actual Flow / Seasonal Design Capability. Data used in these reports lags the current date by at least one month.


Design Flow Capability utilization is a function of several factors that include:

- Total market demand for Alberta natural gas.
- Seasonal changes in market demand for Alberta natural gas.
- Receipt nominating practices of customers individually and in aggregate to meet that level of demand.
- Effect of scheduled maintenance on actual flow requirement in a design area at any given time.
- Design assumptions used in determining required segment flow requirement.

Future Firm Transportation Service Availability


The Future Firm Transportation Service Availability report presents guidelines and timing for all future firm transportation service requests.

NGTL Design Areas

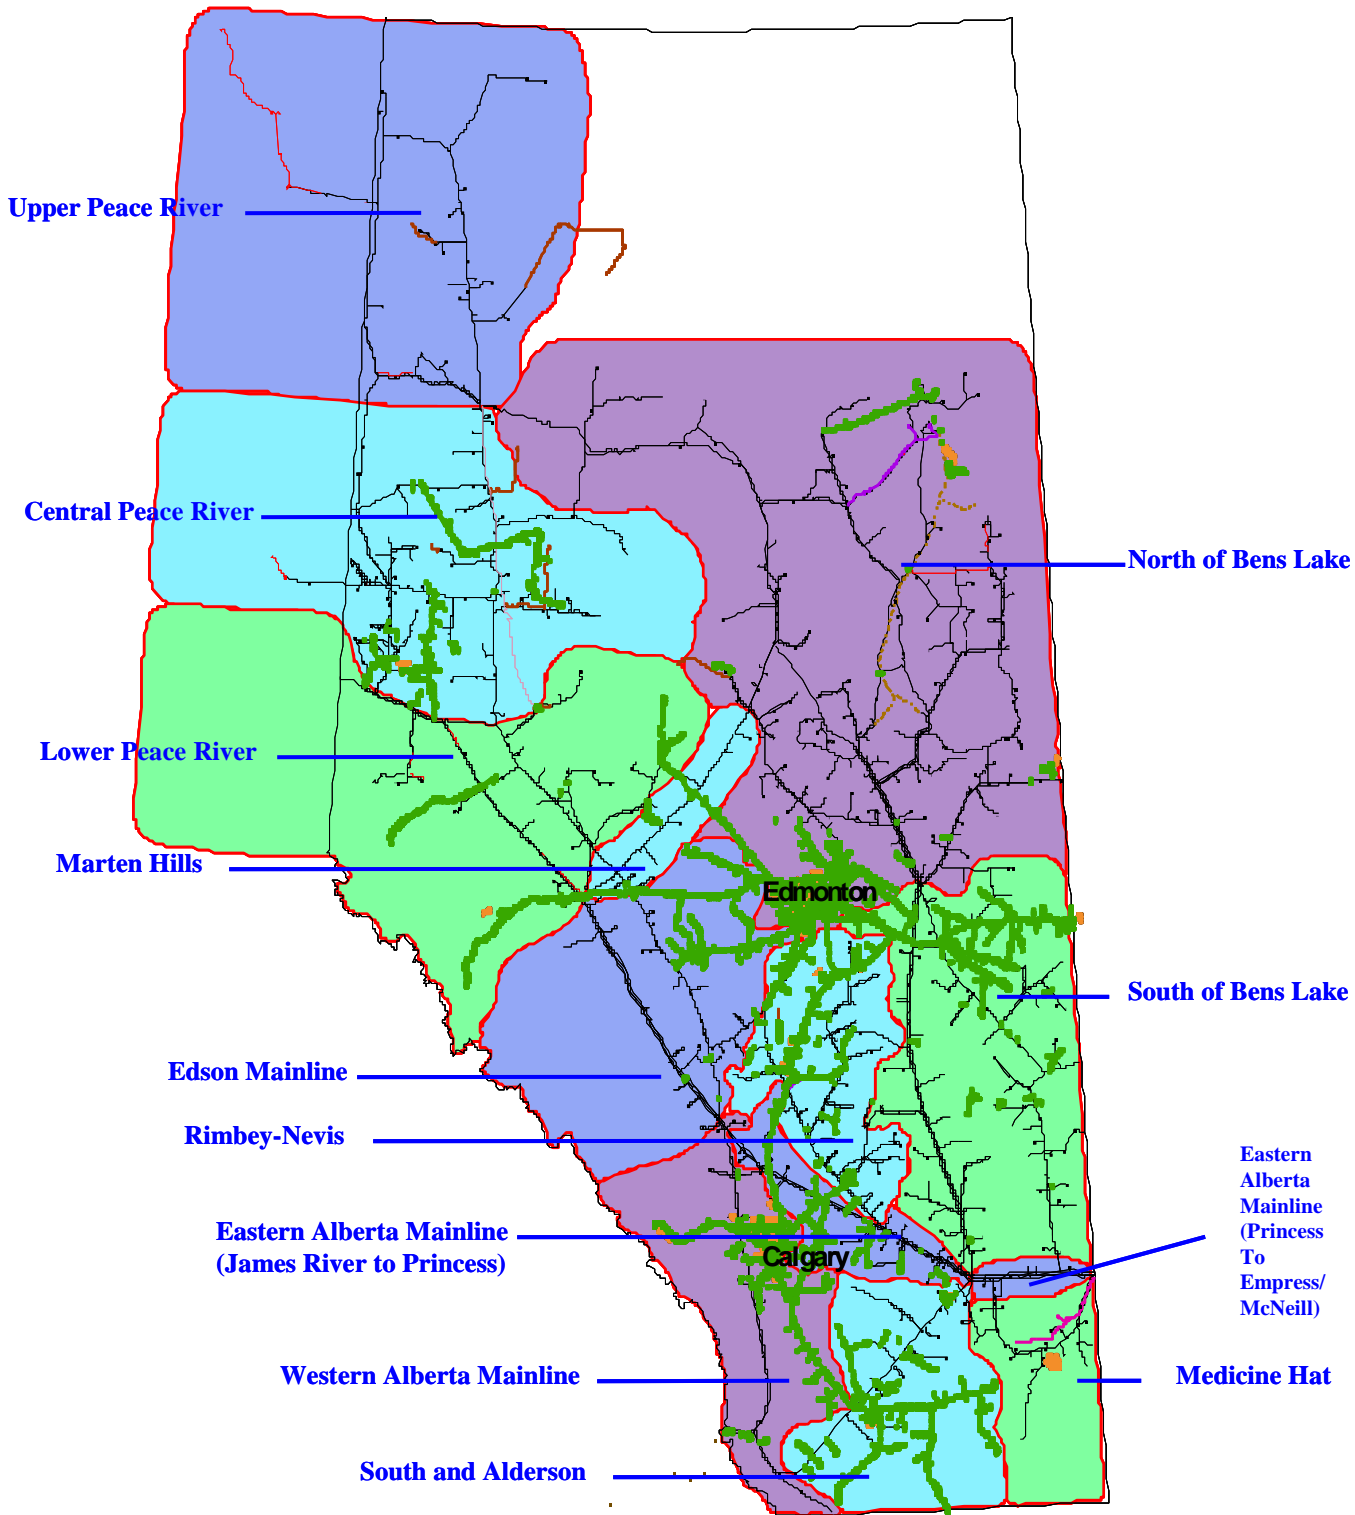

(Last updated Nov 2011)

NGTL Pipeline Segments

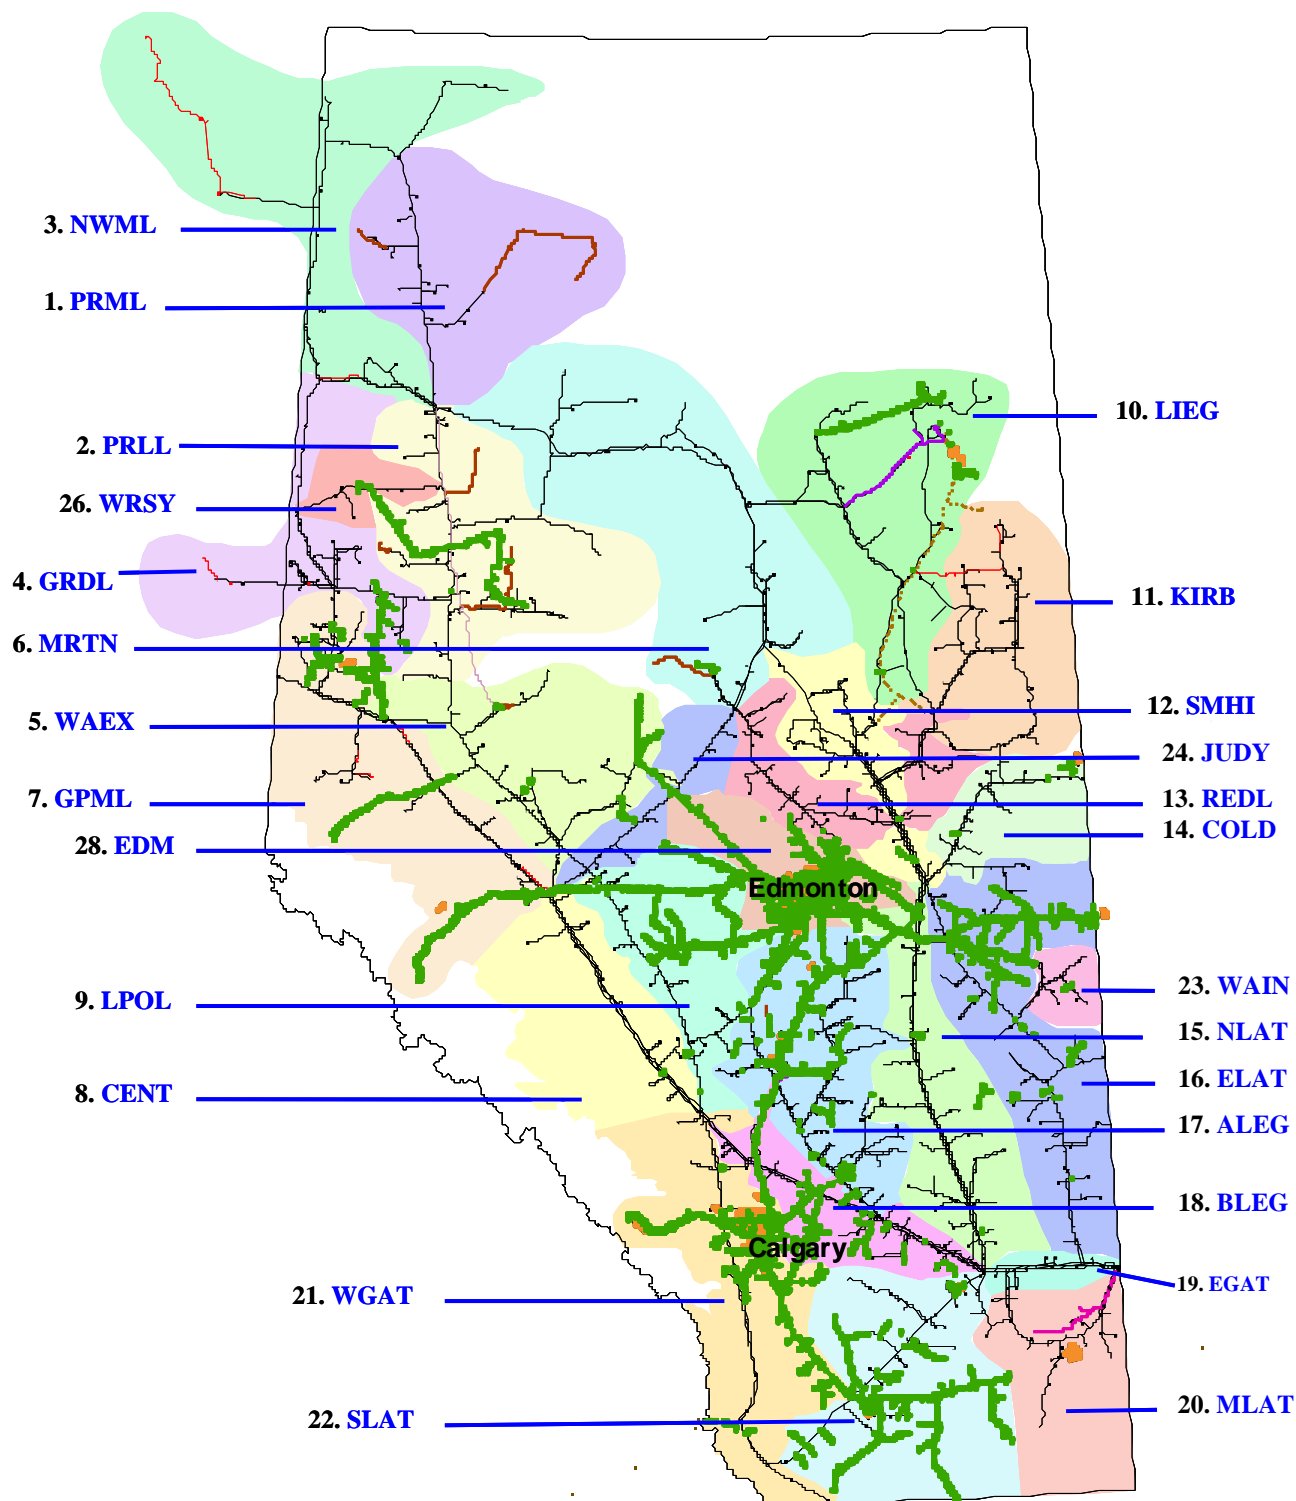

(Last updated Nov 2011)

DEFINITION OF TERMS

Design Capability Utilization

Actual Flow

The amount of gas flowing within or out of our design area.

Design Capability

The volume of gas that can be transported at various points on the pipeline system considering design assumptions.

AVGLF (Average Load Factor)

The ratio between average *Actual Flow* and *Design Capability*. It is calculated for every design season (summer/winter) as shown on the graphs.

Intra NGTL System Deliveries

The amount of sales gas flowing off the system within an area.

Receipt Flow

Aggregate of actual receipts within an area and the *Actual Flow* of the upstream area.

Historical Transportation Service Availability

Average % CD Restricted

The average percentage of the entire segment receipt contract demand restricted during periods of restriction.

Firm Service Restriction

Percentage of time firm service is restricted.

Max % CD Restricted

The maximum percentage to which the entire segment contract demand was restricted.

Firm Service Available

The percentage of time that all requested firm transportation service requests were transported within a segment.

Interruptible Service Available

The percentage of time that interruptible service requests were transported.

Other

System Load Factor

The volume weighted average of the *Average Load Factor* (AVGLF) of all design areas on the system
